

TMJ Clinic CRM — Frontend

Task Breakdown & Estimation


Scope: Authentication module + Lead Creation (stories received so far). More modules will be appended as stories arrive.

Assumed stack: React + TypeScript SPA talking to the NestJS API. Estimates assume 1 frontend developer, hours of focused work.


1. Frontend Application Flow

1.1 App Bootstrap (Session Restore)


Runs every time the app loads — first visit, refresh, or new tab.

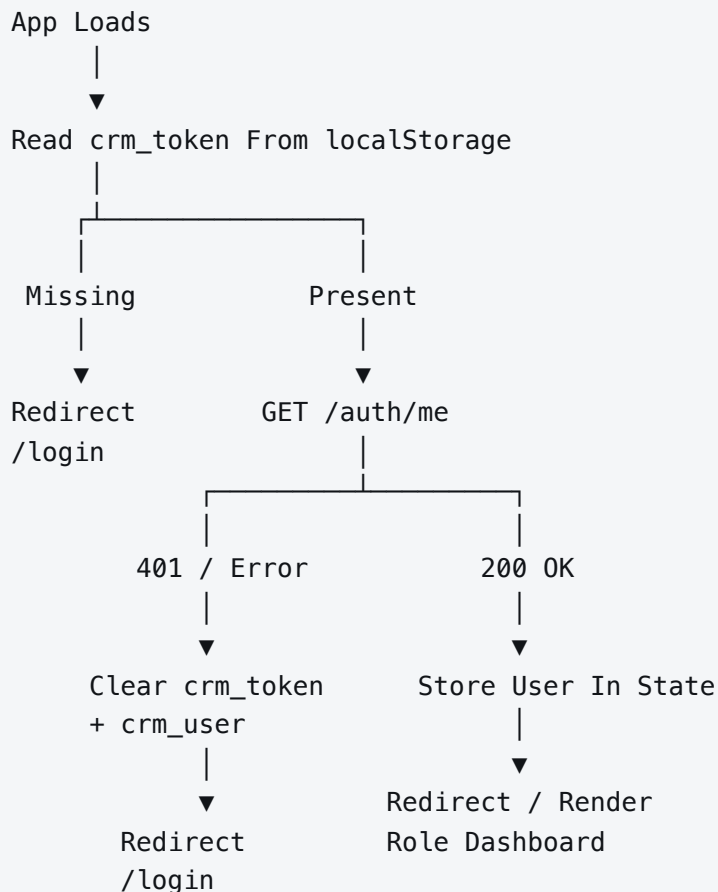


1.2 Login Screen Flow

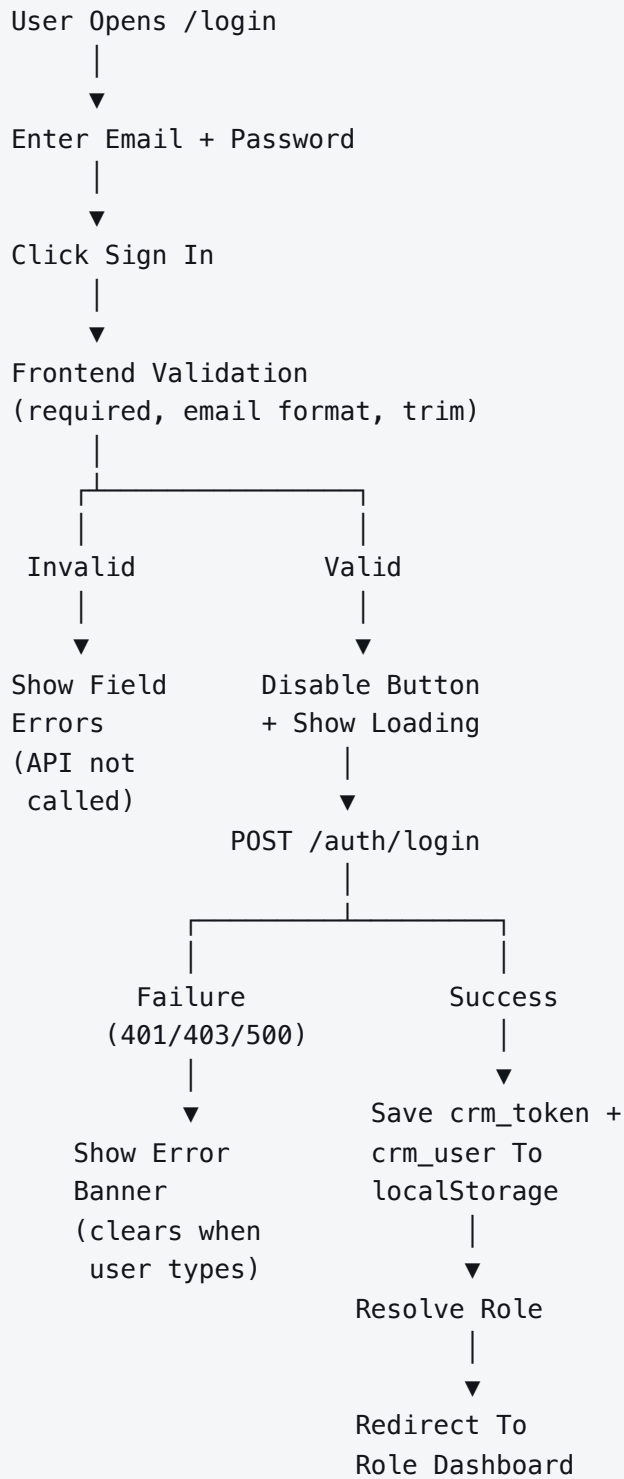

1.3 Route Guard Flow (every protected route)

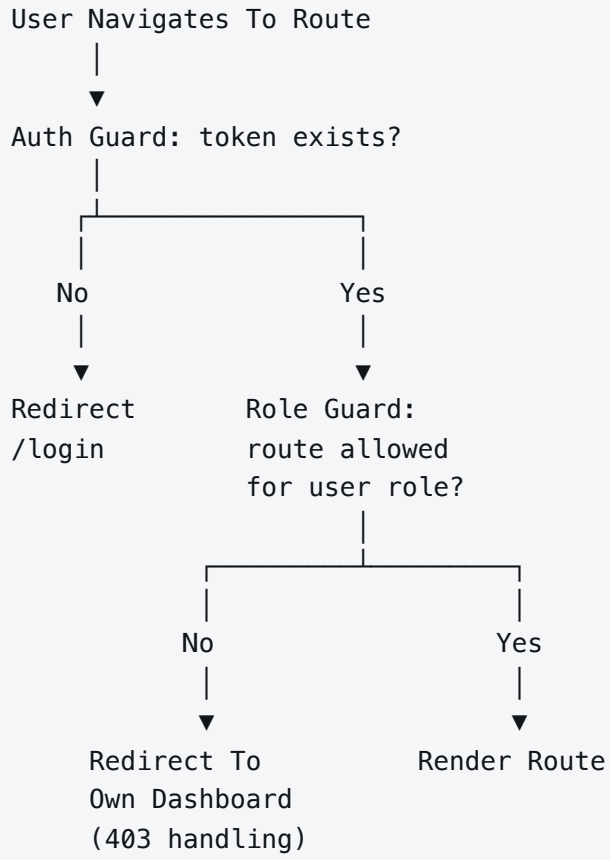

1.4 Add Lead Flow

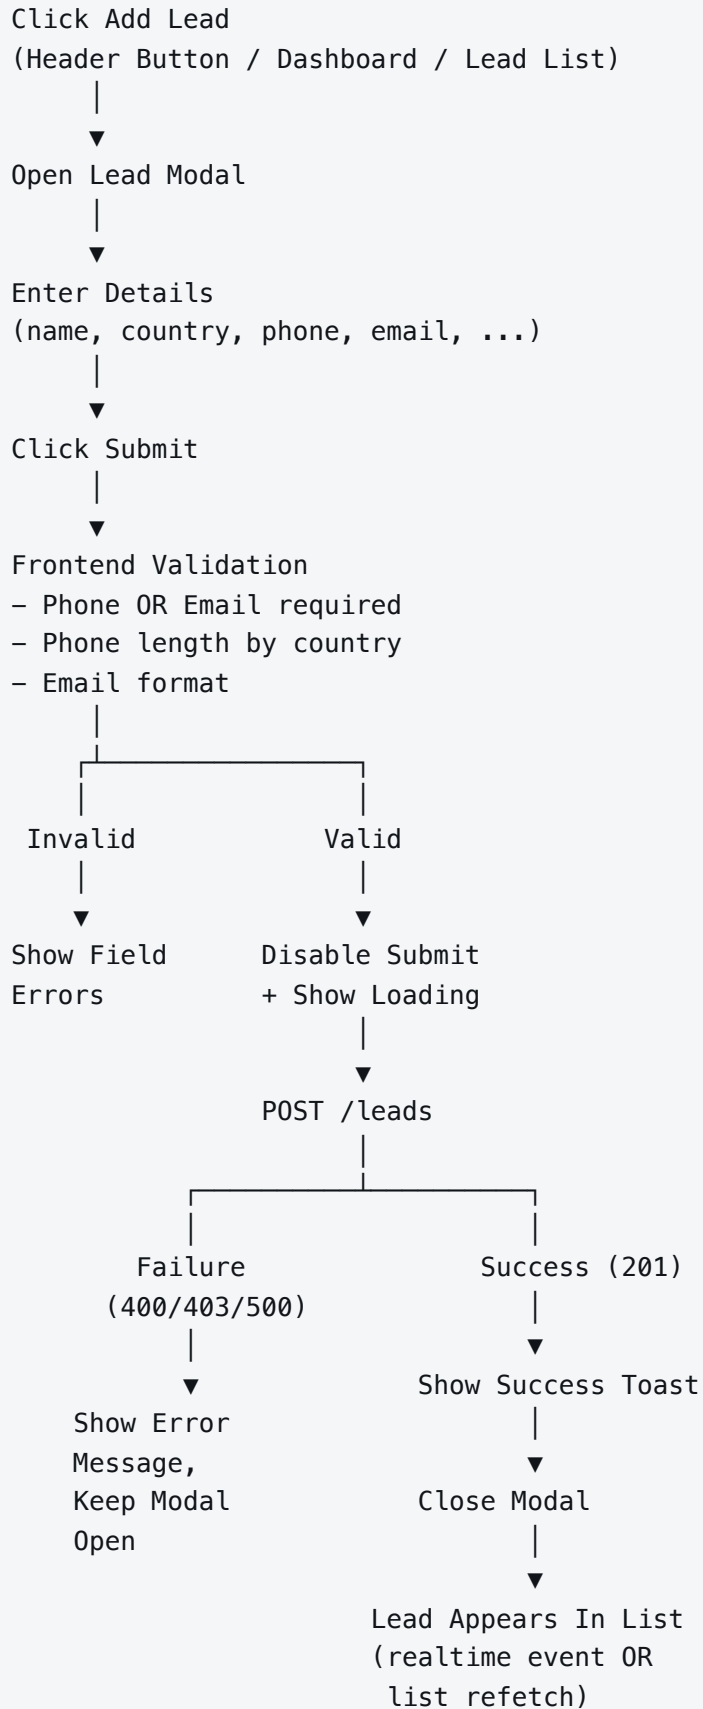

2. Task Breakdown & Estimates

Phase 0 — Foundation (before any module)

ID	TASK	EST (H)	DEPENDS ON
FE-001	Project setup: scaffold, router, folder structure, lint, env config	2	—
FE-002	API client: base fetch/axios wrapper, JWT header injection, global 401 handler	2	FE-001
FE-003	Shared UI kit: Button, Input, Modal, Toast, Error Banner, Loader	4	FE-001
FE-004	Auth store: state management + localStorage sync (crm_token, crm_user)	2	FE-001

Phase 0 subtotal: **10 h**

Phase 1 — Authentication Module

ID	TASK	EST (H)	DEPENDS ON
FE-101	Login page UI: logo, layout, responsive, password visibility toggle	3	FE-003
FE-102	Client-side validation: required fields, email format, max 255, trim	1.5	FE-101
FE-103	Login API integration: loading state, error banner, error clears on typing	2	FE-002, FE-102
FE-104	Role-based redirect after login (5 role dashboards)	1.5	FE-103
FE-105	Auth route guard: unauthenticated users → /login	2	FE-004
FE-106	RBAC route guard: cross-role dashboard access → redirect to own dashboard	2	FE-105
FE-107	Session restore on refresh / new tab (bootstrap + GET /auth/me)	2	FE-004
FE-108	Token expiry handling: any 401 → clear session → redirect /login	1.5	FE-002
FE-109	Logout: clear storage, reset state, redirect /login	1	FE-004
FE-110	Edge cases: double-click submit, browser offline, corrupted localStorage	2	FE-103
FE-111	QA checklist pass + bug fixes (auth module)	2	FE-101...110

Phase 1 subtotal: **20.5 h**

Phase 2 — Lead Creation

ID	TASK	EST (H)	DEPENDS ON
FE-201	Global Add Lead button in header + entry points on dashboard and lead list	1.5	FE-003
FE-202	Add Lead modal UI: form fields, layout, close/cancel without saving	3	FE-003
FE-203	Country selector + phone input with country-based length validation	3	FE-202
FE-204	Phone-OR-email mandatory rule + email format validation	1.5	FE-202
FE-205	Create Lead API integration: submit, loading state, prevent duplicate submit	2	FE-002, FE-204
FE-206	Success flow: toast, close modal, reset form	1	FE-205
FE-207	Realtime subscription: new lead appears in list instantly, reconnect handling	3	FE-205
FE-208	Error handling: 400 / 403 / 500, network timeout, user-friendly messages	1.5	FE-205
FE-209	Edge cases + QA checklist pass (lead creation)	2	FE-201...208

Phase 2 subtotal: **18.5 h**

3. Summary & Timeline

PHASE	SCOPE	HOURS	WORKING DAYS (8H)
Phase 0	Foundation	10	1.3
Phase 1	Authentication	20.5	2.6
Phase 2	Lead Creation	18.5	2.3
–	Buffer (15% — reviews, rework, integration issues)	7.5	0.9
Total	Auth + Lead Creation MVP	56.5	~7 days

Notes on the estimate:


- The buffer covers code review feedback, API contract changes, and integration debugging with the backend.
- FE-207 (realtime) is the riskiest task — the estimate assumes the backend realtime channel (e.g. Supabase / WebSocket / SSE) is already decided and documented. If not, flag it early.
- Phases 1 and 2 can slightly overlap once Phase 0 is done, but a single developer should finish auth guards before lead screens, since every lead screen sits behind them.

4. Tracking

Track each task with this template (copy into your tracker / sheet):

ID	TASK	EST (H)	ACTUAL (H)	STATUS	BLOCKER / NOTES
FE-101	Login page UI	3		Not Started	

Status values:



Working agreement (suggested):

- Update Status + Actual hours daily (end of day).
- A task stays "In Progress" max 2 days — if longer, split it or mark it Blocked with a reason.
- Estimate vs Actual variance > 50% → mention it in standup so future estimates improve.
- Definition of Done: works in the browser, passes the story's QA checklist items, reviewed, merged.
